


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 24, '19	Dec 1, '19	Dec 8, '19	Dec 15, '19	Dec 22, '19	Dec 29, '19	Jan 5, '20	Jan 12, '20	Jan 19, '20	Jan 26, '20
1	☒	Canoa Ranch Site Improvements - 3 Week Look Ahead	35 days	Mon 12/2/19	Thu 1/23/20			S	M	T	W	T	F	S			
2	☒	Safety	35 days	Mon 12/2/19	Thu 1/23/20			S	M	T	W	T	F	S			
3	☒	Mobilization	1 day	Mon 12/2/19	Mon 12/2/19												
4	☒	Survey	3 days	Mon 12/2/19	Wed 12/4/19	3SS											
5	☒	Site Layout / Bootup	3 days	Mon 12/2/19	Wed 12/4/19	4SS											
6	☒	Clearing and Grubbing	5 days	Mon 12/2/19	Fri 12/6/19	5SS	5 ACR										
7	☒	Barbed Wire Fence Install	5 days	Mon 12/9/19	Fri 12/13/19	6											
8	☒	Drainage Excavation	8 days	Mon 12/9/19	Wed 12/18/19	6	14,000 CY										
9	☒	Finish Basin	5 days	Tue 12/17/19	Thu 12/26/19	6											
10	☒	Structure X <i>NEW SPILLWAY</i>	3 days	Mon 12/16/19*	Wed 12/18/19	7											
11	☒	Concrete	2 days	Thu 12/19/19	Fri 12/20/19	10											
12	☒	Landscaping	22 days	Thu 12/19/19	Thu 1/23/20	8											

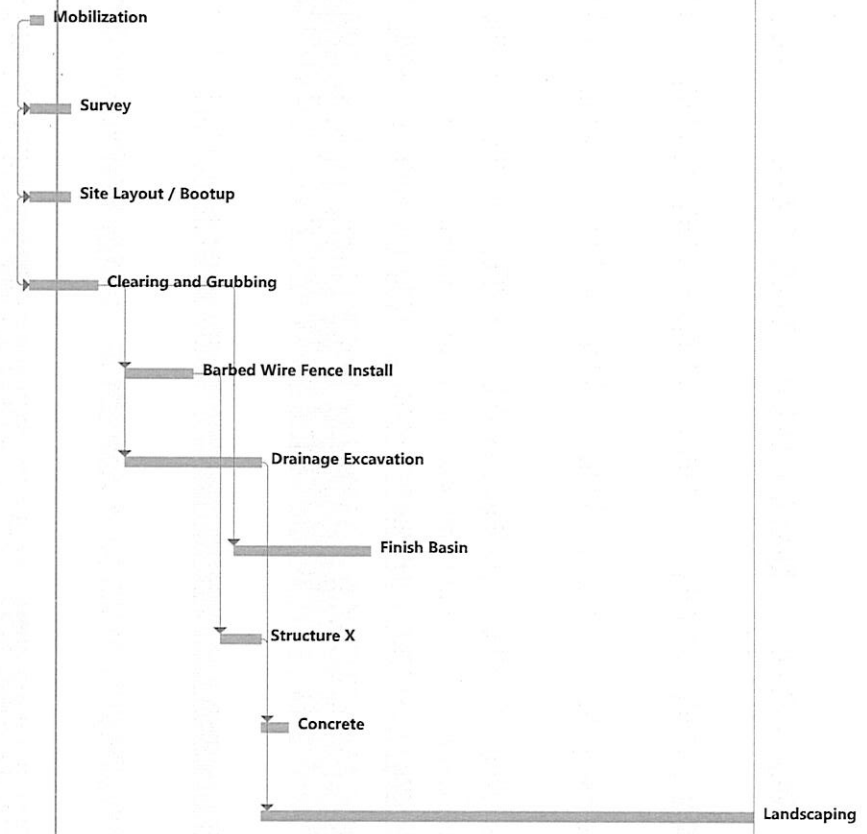

PROPOSED DRAIN DOWN OF AREA @ SPILLWAY

**RUMMEL STATED THAT THE TIME FOR THE CONCRETE WORK + DRAWDOWN CAN BE ADJUSTED IF NRPR WOULD LIKE. OTHERWISE 12/16 IS FIRST AVAIL FOR CREW.*

Project: 3 Week Look Ahead Date: Wed 12/4/19	Task	Project Summary	Manual Task	Start-only	Deadline
	Split	Inactive Task	Duration-only	Finish-only	Progress
	Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
	Summary	Inactive Summary	Manual Summary	External Milestone	

12/5/19 Weekly Field Mtg.
