

PIMA COUNTY TRANSPORTATION ADVISORY COMMITTEE

FY19-20 Pavement Program Update

February 25, 2020

Arterial/Collectors, Regional Priority and Local Roads



www.pima.gov



PIMA COUNTY

Pavement Repair Program Update

Local Roads (27.95 miles):

1. Estrella Subdivision:
 - Paving completed and inspections underway.
2. Green Valley Fairways NO. 3 –
 - Curb Ramps in construction.
 - Paving completion in April 2020
3. Northmanor Subdivision Ramp:
 - Ramp construction to start in March 2020
4. Remaining local roads in design process.
 - Paving scheduled from January to April 2020

Budget	Road Class	Streets/Subdivisions/ District	Length (miles)	Treatment Type	Bid Method	OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE
Local	Local	Countywide Local Package	21.38	M/F	Hard Bid									
Local	Local	Estrella Subdivision	1.69	M/F with ADA	JOC									
Local	Local	Northmanor Subdivision	2.40	M/F with ADA	Paving JOC									
Local	Local	GV Fairways No 3 Subdivision	2.48	M/F with ADA	JOC									
			27.95											

<i>PAVING COMPLETED - AWAITING FINAL INSPECTION AND DOCUMENTATION</i>												
<i>Schedule change due to concrete work</i>												

Project Photos – Estrella Subdivision



Completed Paving Operation



Project Photos – Estrella Subdivision



**Completed Paving
Operation**



Project Photos – Green Valley Fairways NO. 3



Curb Ramp Construction



Pavement Repair Program Update

Arterials/Collectors & Regional Priority (53.67miles)

1. Job Order Contract (JOC) for Arterial/Collectors and RPRG
 - Paving starting January 2020 through June 2020 (end of FY 19/20)
2. Master Agreement for Surface Treatments and Crack Filling
 - In procurement process, treatments completion end of June 2020
3. Unallocated \$4M
 - In procurement process, paving completion end of June 2020
4. Ina Road – Shama Wing to La Cholla Blvd – paving completed
5. Ina Road JOC for extending limits west to CDO Wash Bridge
 - Paving completion in March 2020

Budget	Road Class	Streets/Subdivisions/District	Length (miles)	Treatment Type	Bid Method	OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE
ART/COL & RPRG	Arterial/Collector	D1 - Ina, Mona Lisa, Chula Vista	2.46	M/F	Paving JOC									
ART/COL & RPRG	Arterial/Collector	D4 - Abrego, Continental	3.55	M/F	Paving JOC									
ART/COL & RPRG	Arterial/Collector	D1	3.90	M/F	Paving JOC									
ART/COL & RPRG	Arterial/Collector	D2	4.00	M/F	Paving JOC									
ART/COL & RPRG	Arterial/Collector	D3	5.54	M/F	Paving JOC									
ART/COL & RPRG	Arterial/Collector	D4	2.90	M/F	Paving JOC									
ART/COL & RPRG	Arterial/Collector	D5	6.84	M/F	Paving JOC									
SEALCOAT	Arterial/Collector	Countywide	24.48		MA									
MASTER	Arterial/Collector	Countywide	24.48		MA									
			53.67											

Project Photos – Columbus Blvd and Rex St



Milling and Paving Operations



Project Photos – Columbus Blvd and Rex St



Milling and Paving Operations



Pavement Repair Program Update


\$10M Additional Funding – Local Roadways various BOS Districts (42.28 miles)

1. Green Valley Fairways NO. 2 and Green Valley Desert Meadows NO. 1
 - Curb Ramps in design process.
 - Paving completion end of June 2020
2. Remaining local roadways will be scheduled in March, paving completion end June 2020

Budget	Road Class	Streets/Subdivisions/District	Length (miles)	Treatment Type	Bid Method	OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE
\$10M ADDITIONAL	LOCAL	BOS DIST 1 & 5	17.70	M/F	Hard Bid									
\$10M ADDITIONAL	LOCAL	BOS DIST 2, 3 & 4	21.23	M/F	Hard Bid									
\$10M ADDITIONAL	LOCAL W/ CURB RAMP	GV Fairways No.2 GV Desert Meadows NO. 1	3.35	M/F with ADA	Paving JOC									
			42.28											

Road Repair & Preservation Projects Map

dot.pima.gov Pima County Road Repair and Preservation Projects

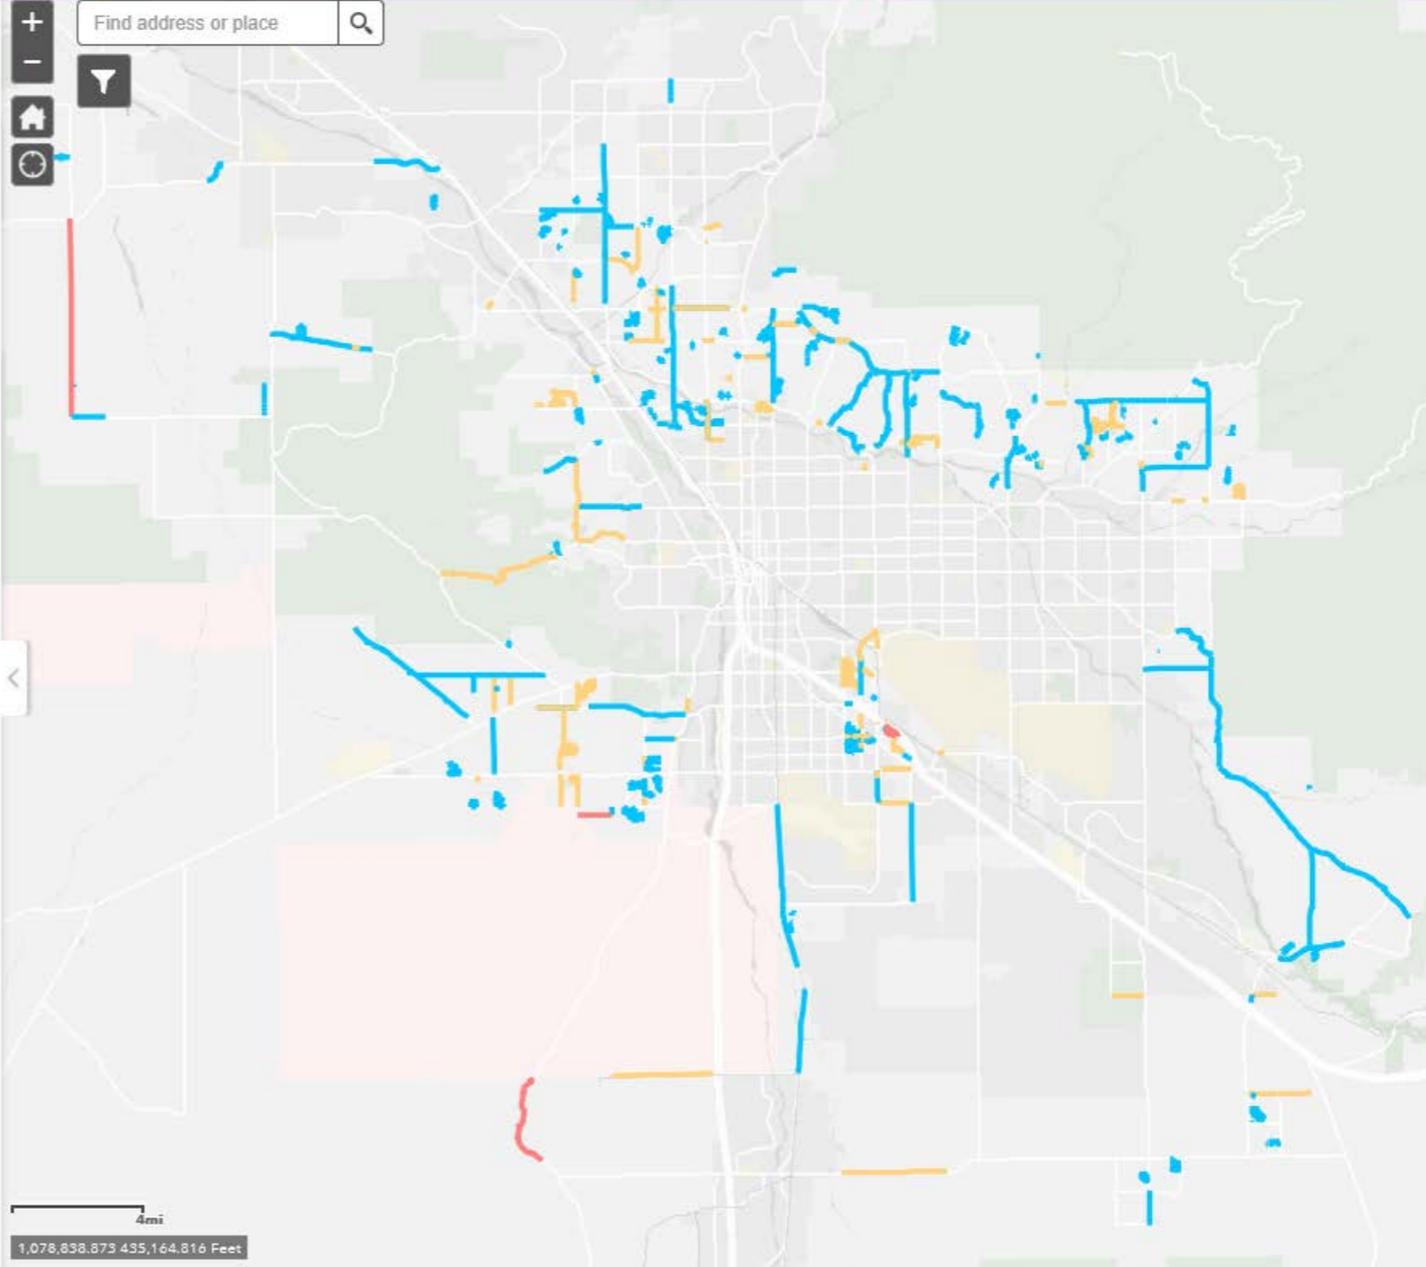



The Road Repair and Preservation Projects Application provides public information about past, current and future roadway improvement projects throughout Unincorporated Pima County.

Past and current projects will be updated as necessary and new [Regional Road Repair Program](#) projects will be added as they are selected.

Use the filter  under the search bar to filter the map by project status and/or project year.

To view the City of Tucson's roadway projects funded by the half-cent sales tax increase, visit [Tucson Delivers](#).

Map Legend:

Road Projects

-  Planned
-  Active Construction
-  Complete

4mi
1,078,838.873 435,164.816 Feet

<http://www.pima.gov/RoadRepairMap>

Discussion

Contact Information:
Robert.Lane2@pima.gov
John.Olivas@pima.gov



www.pima.gov



PIMA COUNTY
