

PIMA COUNTY TRANSPORTATION ADVISORY COMMITTEE

## FY19-20 Pavement Program Update

December 3, 2019

# Arterial/Collectors, Regional Priority and Local Roads



[www.pima.gov](http://www.pima.gov)



# PIMA COUNTY

# Bid Packaging Discussion

## Local Roads:

1. Estrella Subdivision, work ongoing with completion projected in January 2020
2. Green Valley Fairways NO. 3 - Curb Ramps are in design process. Paving expected to be completed in February 2020
3. Northmanor Subdivision out to bid – Expected work completion in April 2020
4. Remaining local roads awarded – completion by end of FY19/20.


## Arterials/Collectors & Regional Priority

1. 3 JOC packages prepared and awarded or presently out to bid, covering Arterial/Collectors and RPRG roadways in various BOS districts.
2. 5 additional JOC packages currently in preparation which will complete the remaining FY 19/20 Arterial/Collectors and RPRG roadways
3. Master Agreement for surface treatments and crack filling packages being prepared for submittal with work completion by end of FY19/20

## \$10M additional funding – Local Roadways various BOS Districts

1. At least 3 packages are expected to advertise in December 2019

# Project Photos – Anway Road From Manville Road to Avra Valley Road

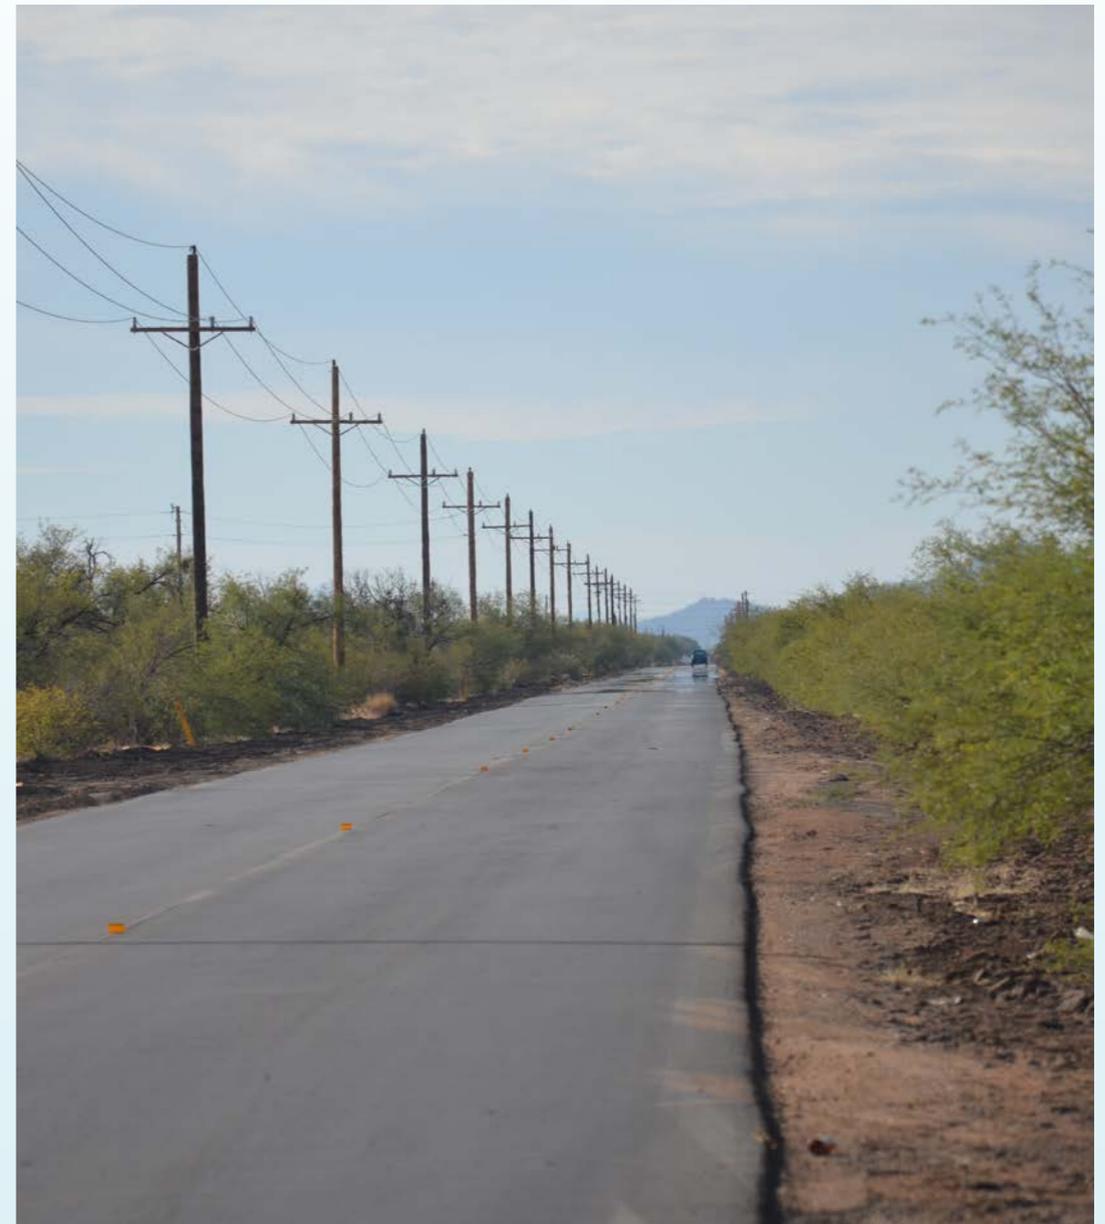

\*Photos courtesy of PCDOT-Project Delivery

# Project Photos – La Cholla Road From Limewood Drive to Moore Road



# Project Photos – Overton Road From Thornydale Road to Shiraz Place



\*Photos courtesy of PCDOT-Project Delivery

# Project Photos – Bear Canyon Road City Limits to the north end



\*Photos courtesy of PCDOT-Project Delivery

# Project Photos – Pinto Lane & Avenida Del Oro



\*Photos courtesy of PCDOT-Project Delivery

# Project Photos – Estrella Subdivision



# Project Photos – Estrella Subdivision



# Road Repair & Preservation Projects Map

dot.pima.gov Pima County Road Repair and Preservation Projects



The Road Repair and Preservation Projects Application provides public information about past, current and future roadway improvement projects throughout Unincorporated Pima County.


Past and current projects will be updated as necessary and new [Regional Road Repair Program](#) projects will be added as they are selected.

To view the City of Tucson's roadway projects funded by the half-cent sales tax increase, visit [Tucson Delivers](#).

**Map Legend:**

**Road Projects**


- Planned
- Active Construction
- Complete

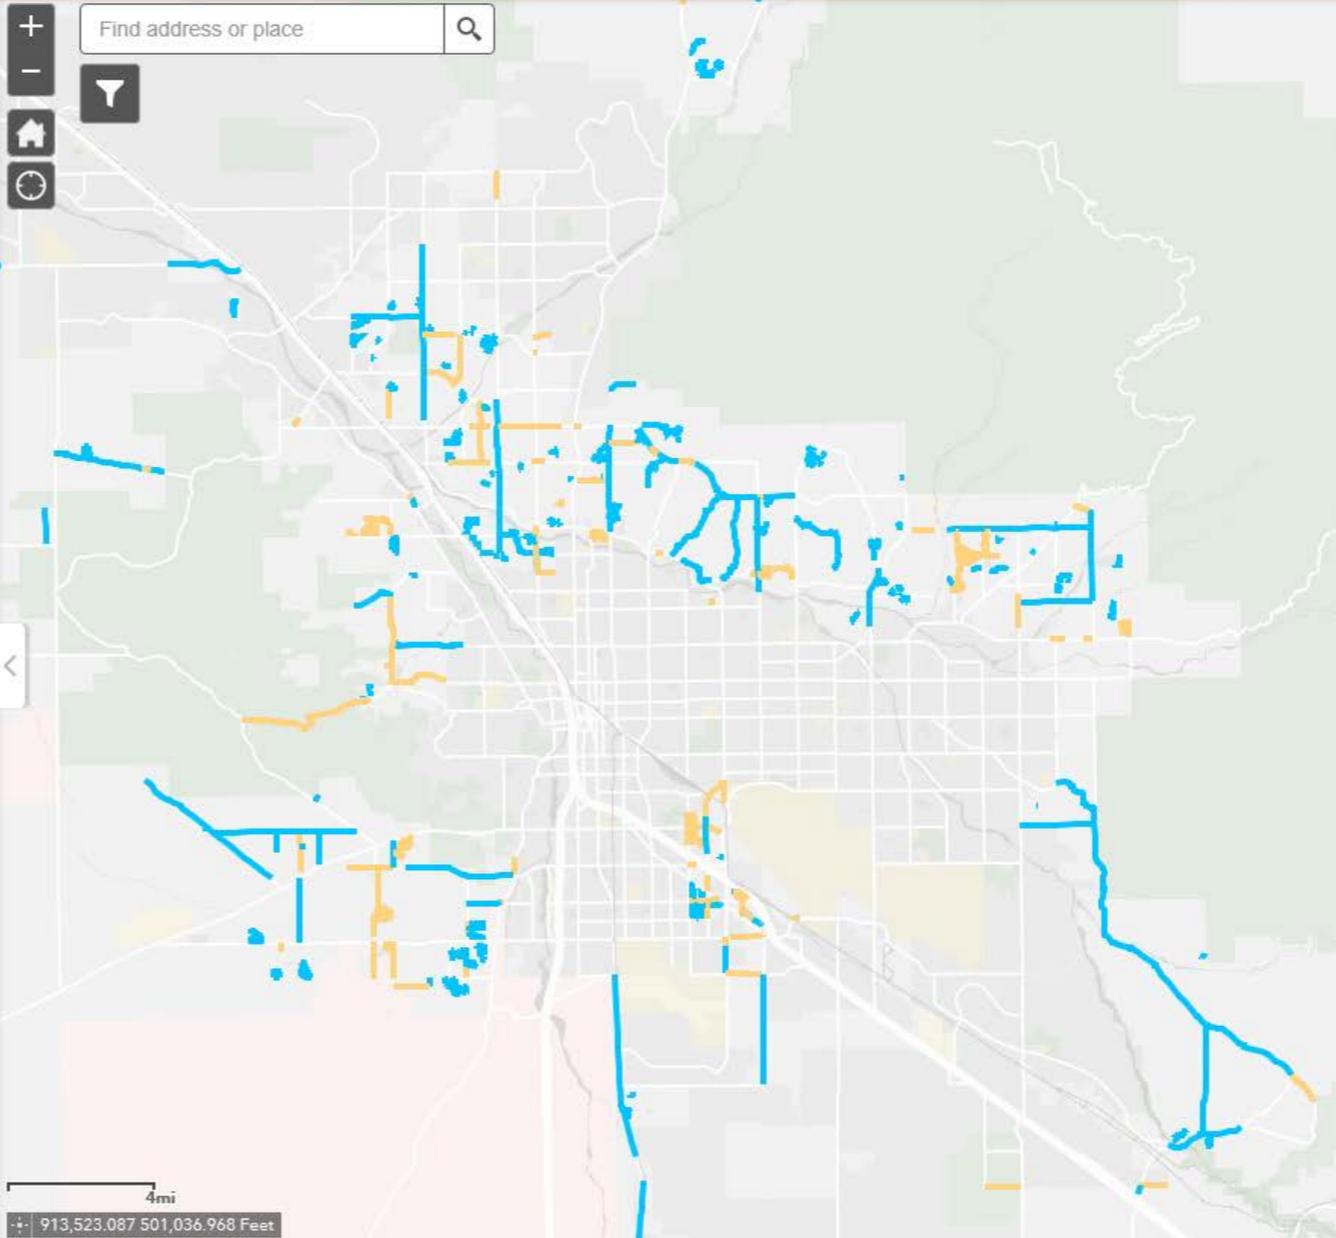

4mi  
913,523.087 501,036.968 Feet

[Road Repair and Preservation Projects Map](#)

# Visualization App

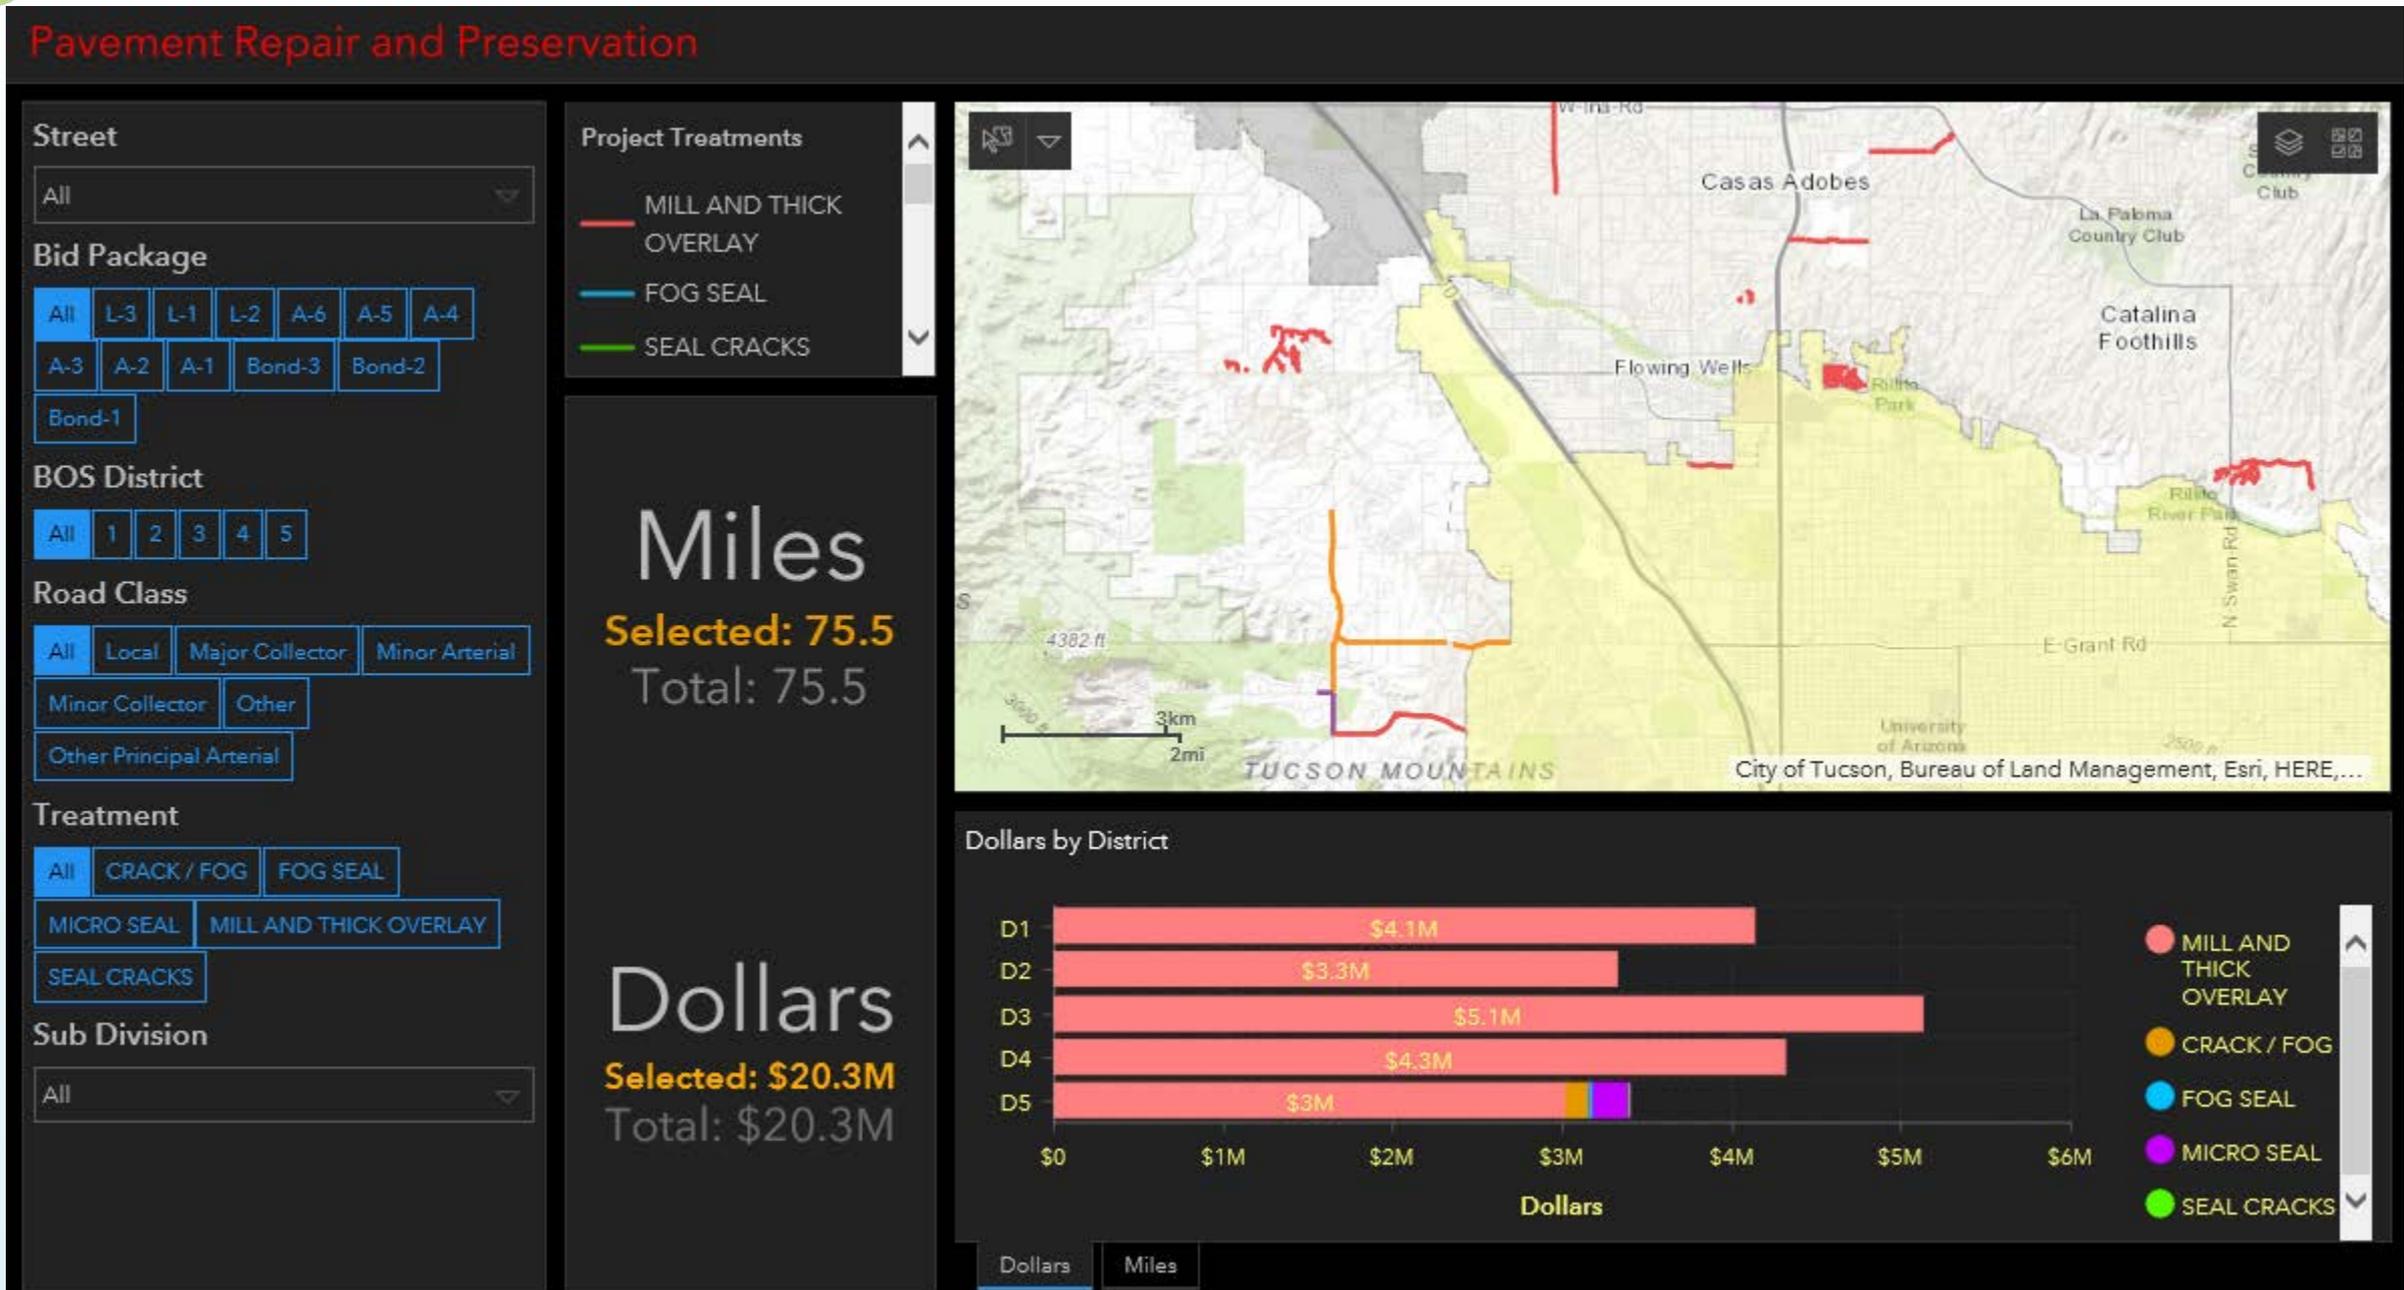

[Bid Packaging Visualization Map](#)

# Discussion

Contact Information:  
Robert.Lane2@pima.gov  
John.Olivas@pima.gov



[www.pima.gov](http://www.pima.gov)



# PIMA COUNTY
